Sketch of LArIAT Installation/ Commissioning

A. Hahn

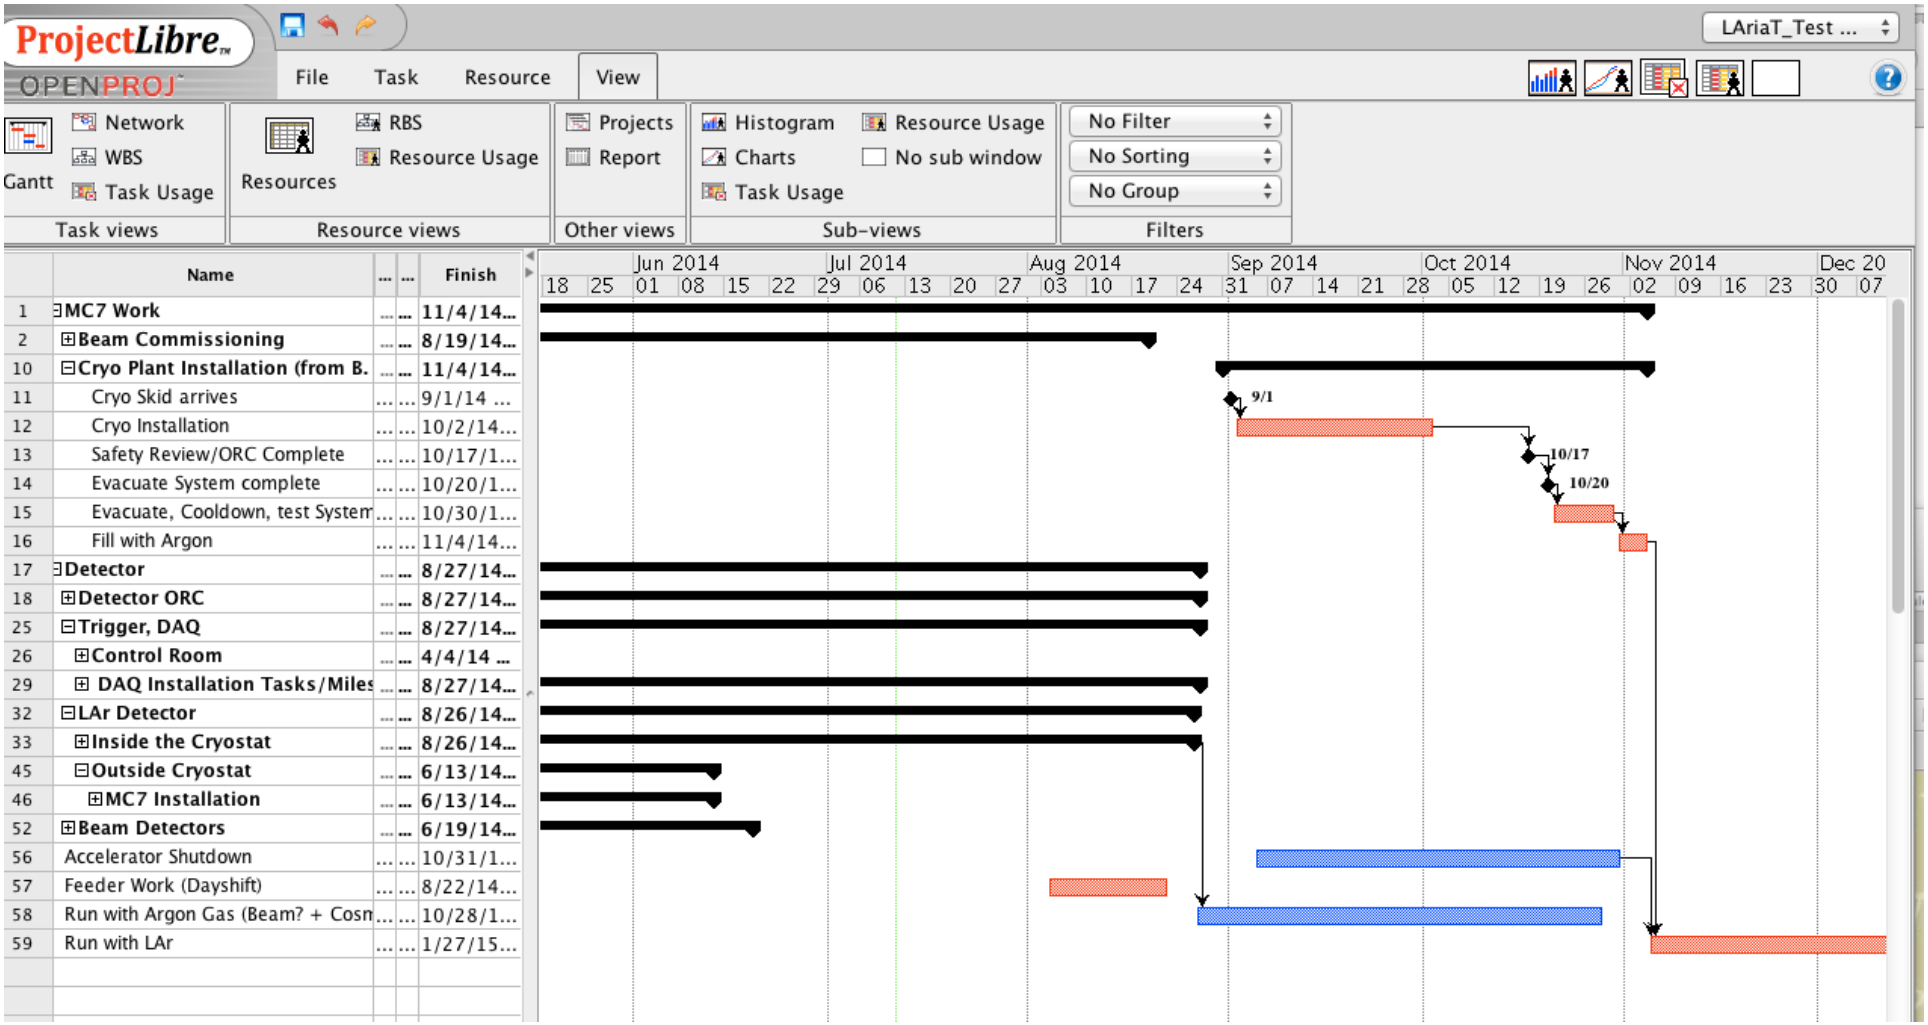
ProjectLibre
OPENPROJ
File
Task
Resource
View
LAriaT_Test ...
Gantt
Network
WBS
Task Usage
Task views
Resources
RBS
Resource Usage
Resource views
Projects
Report
Other views
Histogram
Charts
Task Usage
Resource Usage
No sub window
Sub-views
No Filter
No Sorting
No Group
Filters
Name
Finish
1 MC7 Work 11/4/14...
2 Beam Commissioning 8/19/14...
10 Cryo Plant Installation (from B. 11/4/14...
11 Cryo Skid arrives 9/1/14 ...
12 Cryo Installation 10/2/14...
13 Safety Review/ORC Complete 10/17/1...
14 Evacuate System complete 10/20/1...
15 Evacuate, Cooldown, test System 10/30/1...
16 Fill with Argon 11/4/14...
17 Detector 8/27/14...
18 Detector ORC 8/27/14...
25 Trigger, DAQ 8/27/14...
26 Control Room 4/4/14 ...
29 DAQ Installation Tasks/Miles 8/27/14...
32 LAr Detector 8/26/14...
33 Inside the Cryostat 8/26/14...
45 Outside Cryostat 6/13/14...
46 MC7 Installation 6/13/14...
52 Beam Detectors 6/19/14...
56 Accelerator Shutdown 10/31/1...
57 Feeder Work (Dayshift) 8/22/14...
58 Run with Argon Gas (Beam? + Cosm 10/28/1...
59 Run with LAr 1/27/15...
Jun 2014
Jul 2014
Aug 2014
Sep 2014
Oct 2014
Nov 2014
Dec 20
9/1
10/17
10/20

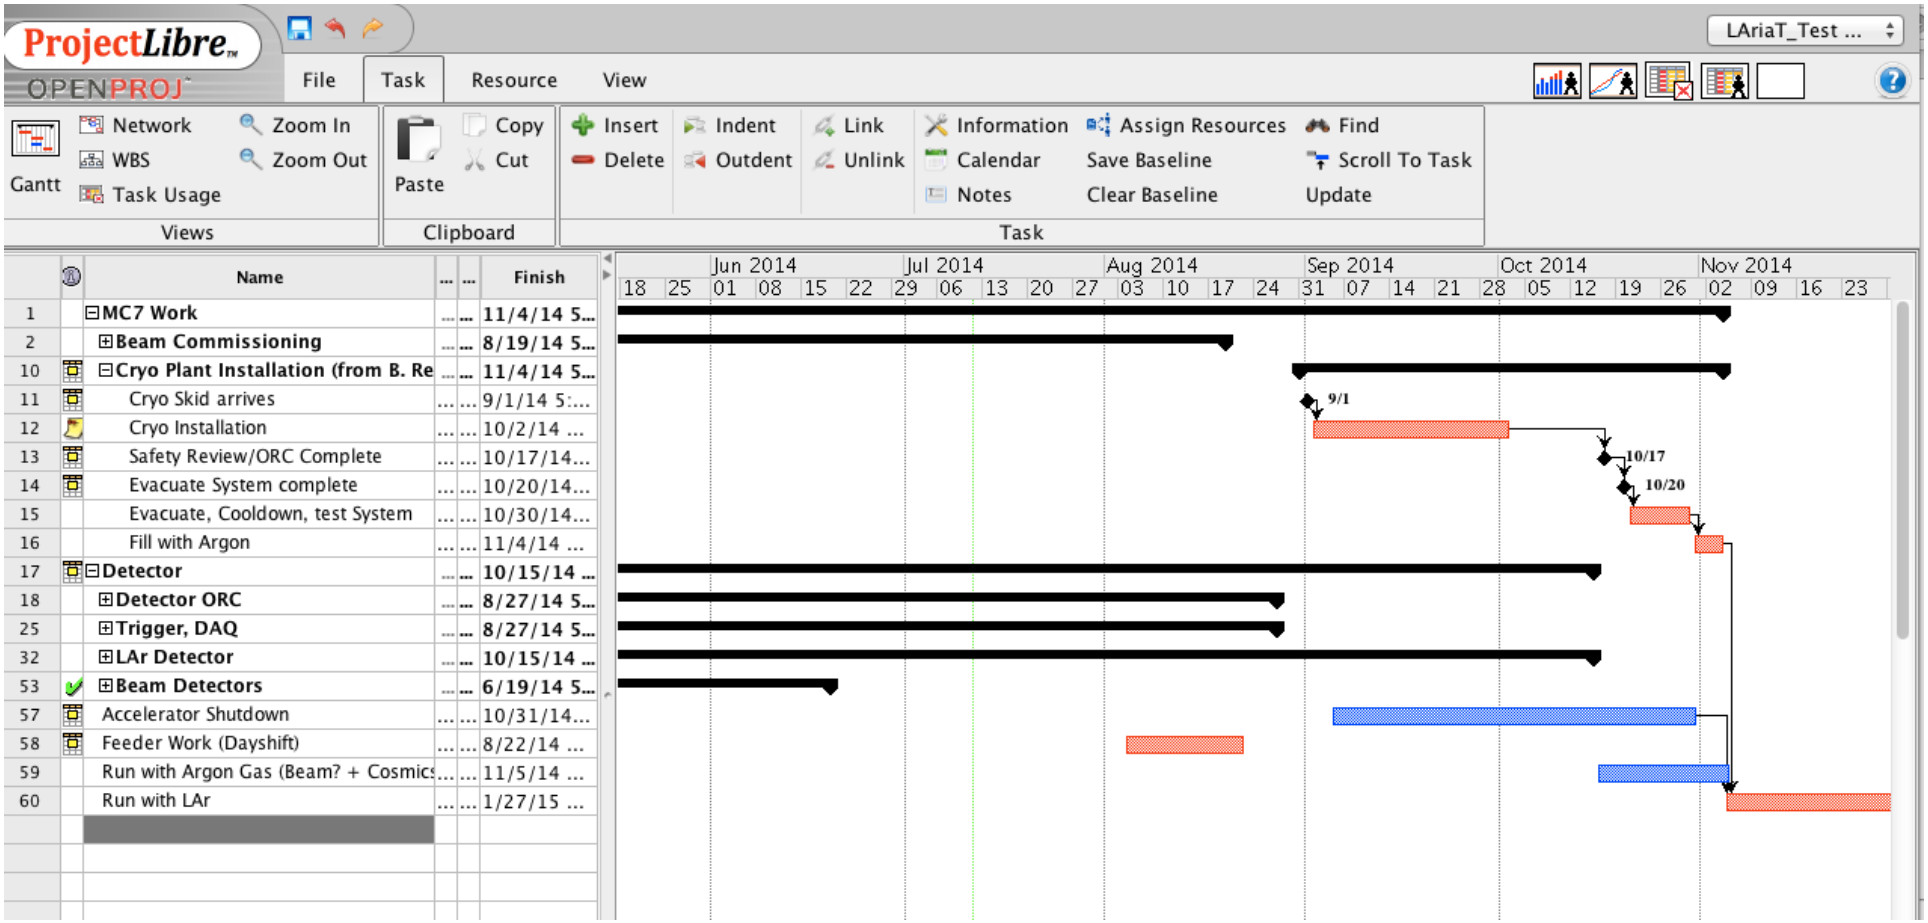
ProjectLibre
OPENPROJ
LAriaT_Test ...
File
Task
Resource
View
Gantt
Network
WBS
Task Usage
Zoom In
Zoom Out
Views
Paste
Copy
Cut
Clipboard
Insert
Delete
Indent
Outdent
Link
Unlink
Information
Calendar
Notes
Assign Resources
Save Baseline
Clear Baseline
Find
Scroll To Task
Update
Task
Name
Finish
1 MC7 Work 11/4/14 5...
2 Beam Commissioning 8/19/14 5...
10 Cryo Plant Installation (from B. Re 11/4/14 5...
11 Cryo Skid arrives 9/1/14 5:...
12 Cryo Installation 10/2/14 ...
13 Safety Review/ORC Complete 10/17/14...
14 Evacuate System complete 10/20/14...
15 Evacuate, Cooldown, test System 10/30/14...
16 Fill with Argon 11/4/14 ...
17 Detector 10/15/14 ...
18 Detector ORC 8/27/14 5...
25 Trigger, DAQ 8/27/14 5...
32 LAr Detector 10/15/14 ...
53 Beam Detectors 6/19/14 5...
57 Accelerator Shutdown 10/31/14...
58 Feeder Work (Dayshift) 8/22/14 ...
59 Run with Argon Gas (Beam? + Cosmics 11/5/14 ...
60 Run with LAr 1/27/15 ...
Jun 2014
Jul 2014
Aug 2014
Sep 2014
Oct 2014
Nov 2014
9/1
10/17
10/20
